








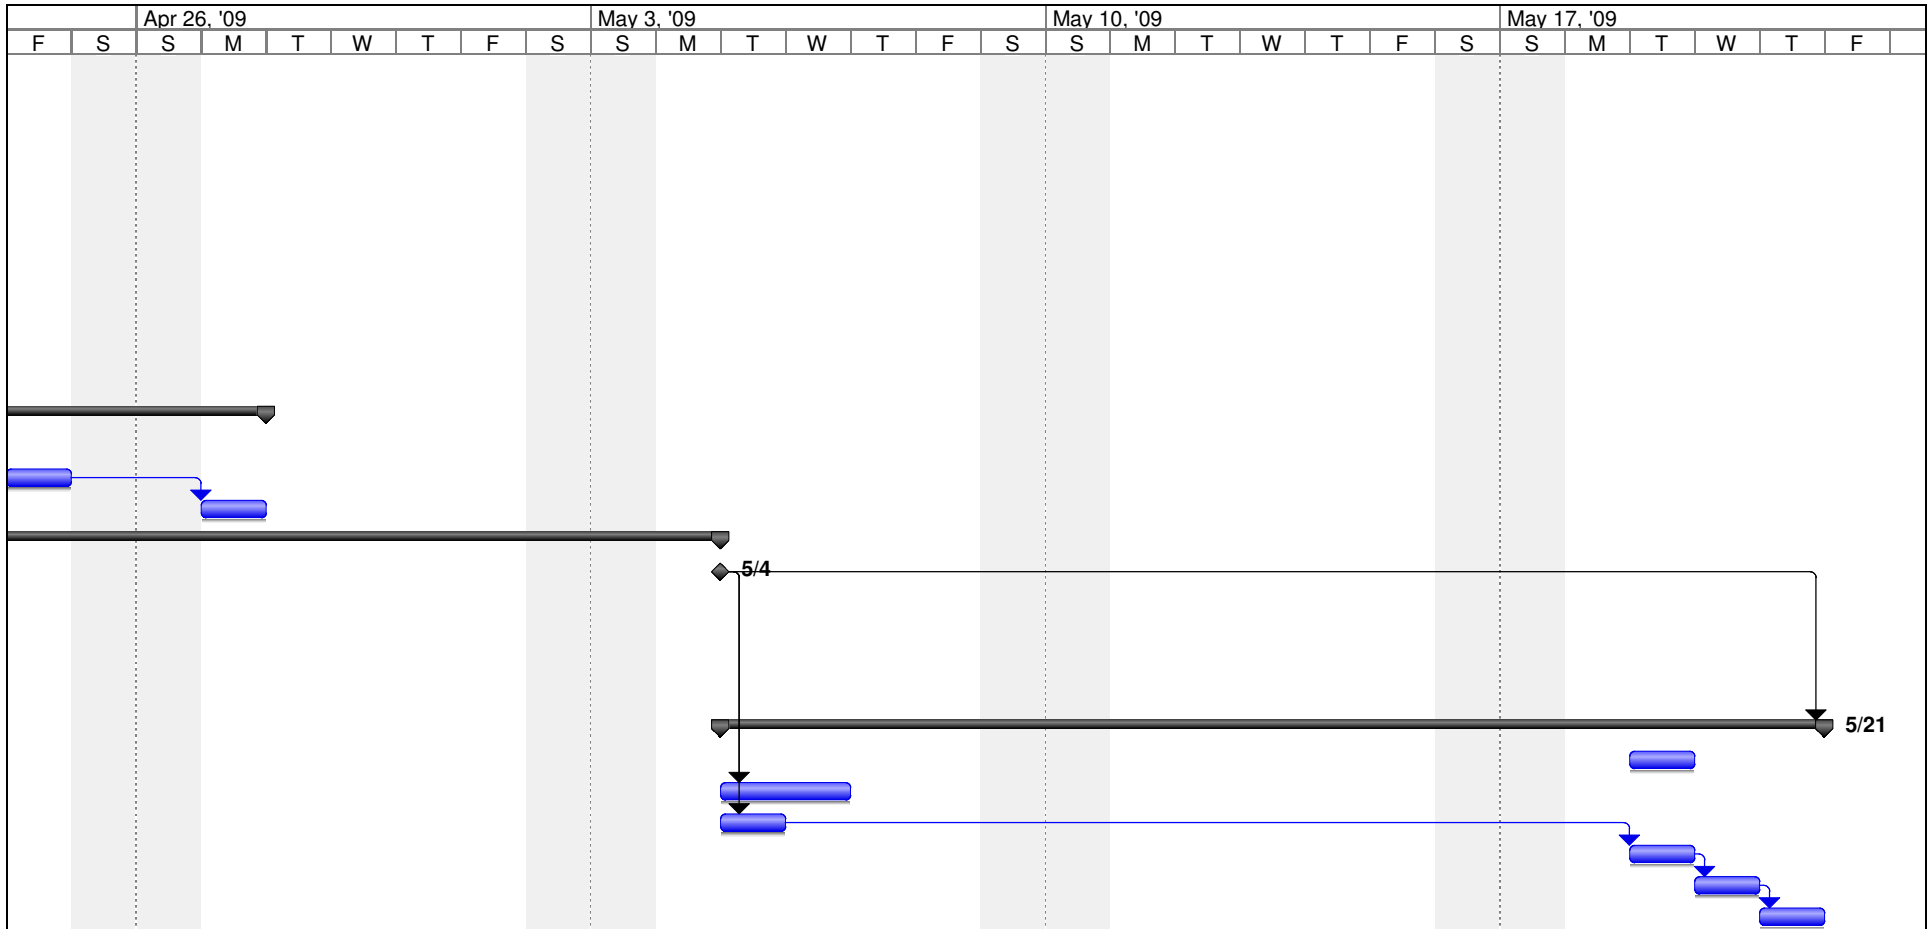


ID	Task Name	Duration	Start	Finish	'09							Apr 19, '09				
					M	T	W	T	F	S	S	M	T	W	T	
1	Site Set-up and Material Delivery	1 day	Tue 4/14/09	Tue 4/14/09												
2	Site meeting and design review	1 day	Tue 4/14/09	Tue 4/14/09												
3	Tear out of kitchen and removal of debris	1 day	Wed 4/15/09	Wed 4/15/09												
4	Frame out new wall	1 day	Thu 4/16/09	Thu 4/16/09												
5	Electrical rough in	1 day	Fri 4/17/09	Fri 4/17/09												
6	Electrical Inspection (permit)	1 day	Fri 4/17/09	Fri 4/17/09												
7	Plumbing & gas relocation	1 day	Mon 4/20/09	Mon 4/20/09												
8	Install insulation, drywall and tape	1 day	Tue 4/21/09	Tue 4/21/09												
9	Install hardwood floors	1 day	Wed 4/22/09	Wed 4/22/09												
10	Site inspection for quality	1 day	Thu 4/23/09	Thu 4/23/09												
11	Cover floors after inspection	1 day	Wed 4/22/09	Wed 4/22/09												
12	Install kitchen cabinetry	3 days	Thu 4/23/09	Mon 4/27/09												
13	Day 1 of Kitchen installation (base cabinets)	1 day	Thu 4/23/09	Thu 4/23/09												
14	Day 2 Of Kitchen installation (upper cabinets)	1 day	Fri 4/24/09	Fri 4/24/09												
15	Day 3 of kitchen installation (install hardware)	1 day	Mon 4/27/09	Mon 4/27/09												
16	Site inspection for quality and counter top template	15 days	Tue 4/14/09	Mon 5/4/09												
17	Finalize counter top quote and production	15 days	Tue 4/14/09	Mon 5/4/09												
18	Sand and prime all walls (prep for paint)	4 days	Tue 4/14/09	Fri 4/17/09												
19	Paint, ceiling, walls and trim	2 days	Tue 4/14/09	Wed 4/15/09												
20	Removal of all additional materials and waste from site	1 day	Thu 4/16/09	Thu 4/16/09												
21	Site review and quality inspection	1 day	Fri 4/17/09	Fri 4/17/09												
22	Counter top installation	13 days	Tue 5/5/09	Thu 5/21/09												
23	Plumbing & Gas reconnection	1 day	Tue 5/19/09	Tue 5/19/09												
24	Tile back splash installation	2 days	Tue 5/5/09	Wed 5/6/09												
25	Electrical finish and move appliances into place	1 day	Tue 5/5/09	Tue 5/5/09												
26	Site clean-up	1 day	Tue 5/19/09	Tue 5/19/09												
27	Final decoration / fixture placements	1 day	Wed 5/20/09	Wed 5/20/09												
28	Final inspection	1 day	Thu 5/21/09	Thu 5/21/09												

Project: Actual Time Line Date: Sun 9/13/09	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	



Project: Actual Time Line Date: Sun 9/13/09	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	
